


PRECAST RIGID FRAME SECTION

3/8" = 1'-0"

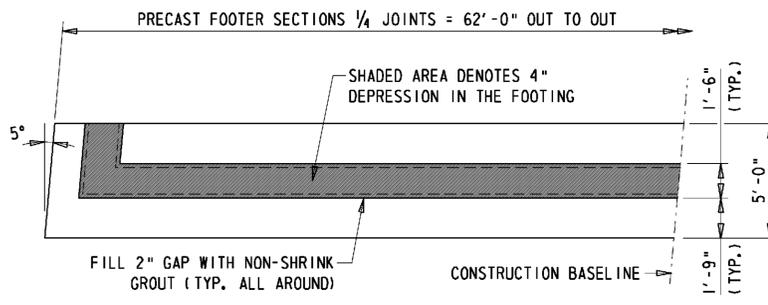


PRECAST FOOTER HALF PLAN

1/4" = 1'-0"


CONTRACT SPECIFIC NOTES

1. THIS CONTRACT SHALL PROVIDE PRECAST ELEMENTS FOR THE REPLACEMENT OF BRIDGE 3-463.
2. FULL BRIDGE PLANS ARE STILL IN DEVELOPMENT AT THE TIME OF BIDDING FOR THIS CONTRACT. IF ADDITIONAL INFORMATION IS NEEDED, PLEASE CONTACT DELDOT CONTRACT ADMINISTRATION.
3. SUPPLIER IS TO SUPPLY AND DELIVER THE PRECAST ELEMENTS TO THE JOB SITE WHICH IS IN ZIP CODE 19975. THE SUPPLIER SHALL COORDINATE WITH THE CONSTRUCTION CONTRACTOR (ONCE CHOSEN BY THE DEPARTMENT) FOR DELIVERY. THE FABRICATOR MUST COORDINATE WITH THE CONSTRUCTION CONTRACTOR WITHIN TWO DAYS OF WHEN THE PRECAST ELEMENTS ARE READY FOR DELIVERY. THE SUPPLIER MUST BE PREPARED TO DELIVER THE PRECAST ELEMENTS TO THE SITE ON MARCH 15, 2013. IF THE SUPPLIER CANNOT MEET THIS DATE, THEN HE SHALL PROVIDE THE EARLIEST DATE IN WHICH HE CAN PROVIDE THE PRECAST ELEMENTS. THE CONSTRUCTION CONTRACTOR SHALL BE RESPONSIBLE FOR OFFLOADING THE PRECAST ELEMENTS FROM THE TRUCKS AT THE SITE. PRECAST ELEMENTS SHALL BE MANUFACTURED IN ACCORDANCE WITH SECTION 602 OF THE STANDARD SPECIFICATIONS.




HEADWALL DETAIL

1/2" = 1'-0"

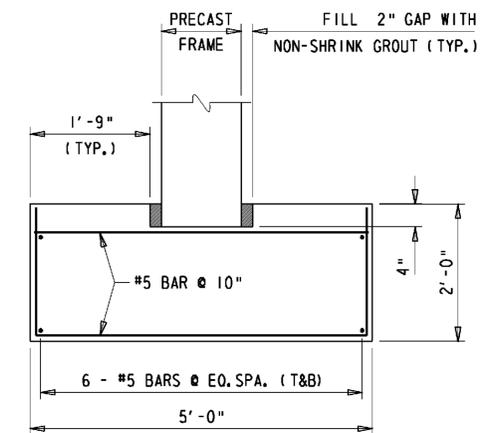


PRECAST FOOTER SECTION

3/4" = 1'-0"

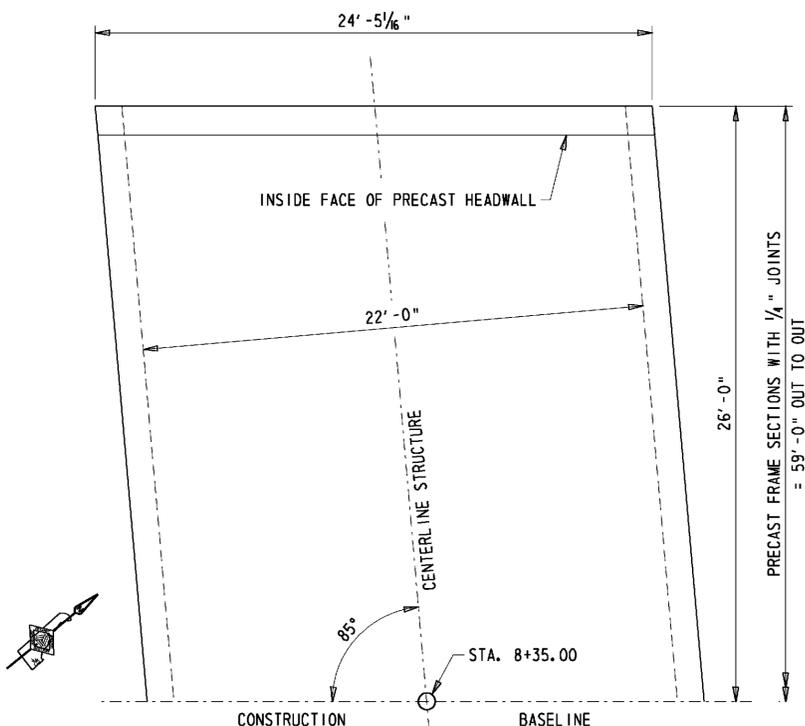


PRECAST RIGID FRAME HALF PLAN

1/4" = 1'-0"

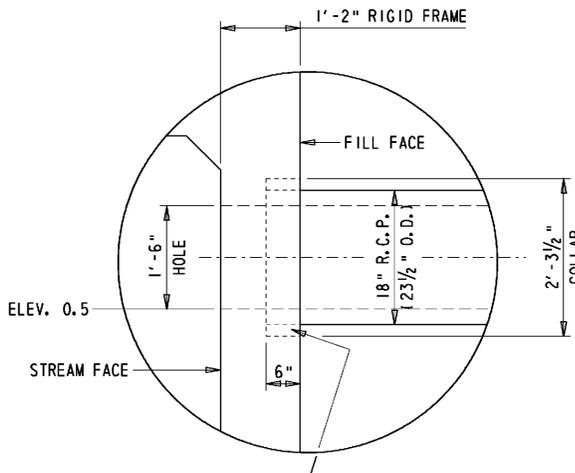

PIPE COLLAR DETAIL


1/2" = 1'-0"

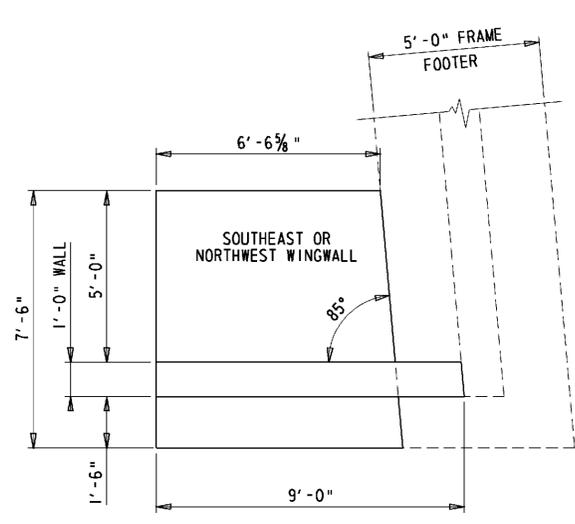

WINGWALL PLAN

3/8" = 1'-0"

F.F. - DENOTES FILL FACE
S.F. - DENOTES STREAM FACE
E.F. - DENOTES EACH FACE

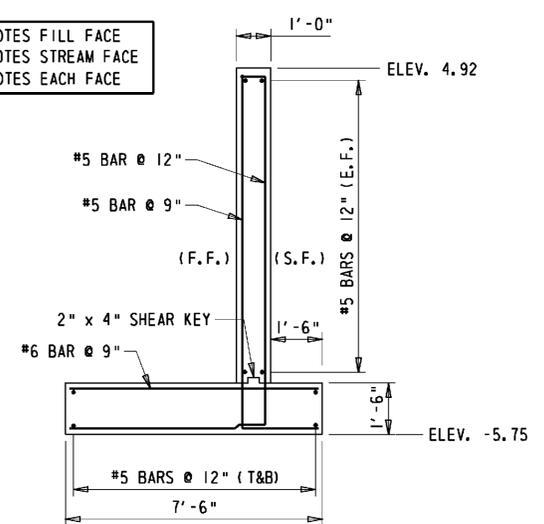

PRECAST WINGWALL SECTION

3/8" = 1'-0"
